BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

PREMEASUREMENT SHEET

Second & Final Bill

Client		**Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064**							
Chainage in m		**Description of Item**	**Unit**	**No**	**Length (m)**	**Breadth (m)**	**Depth (m)**	**Quantity**	**Remarks**
From	**To**								
Item No. 3		Cost of Haulage Excluding Loading and Unloading MORTH -100/ Chapter 1 Case-1: Surface Road .As per the direction of the Engineer Incharge							
Measurement Taken on		10/1/23							
		Quantity Measured in 1st RA Bill	**t.km**					**70.72**	
		Quantity Vide from Item No E9	t.km		60.58	1.28		77.54	
							Total Executed Quantity	**148.26**	
							Quantity Carried to Summary	**148.26**	

CONTRACTOR

PMC

ASSISTANT ENGINEER

ASSISTANT EXECUTIVE ENGINEER

Scanned by TapScanner

Scanned by TapScanner

SECOND AND FINAL BILL

BRUHAT BANGALORE MAHANAGARA PALIKE									
NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency									
PREMEASUREMENT SHEET									
Client		**Second & Final Bill** Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064							
Chainage in m		**Description of Item**	**Unit**	**No**	**Length (m)**	**Breadth (m)**	**Depth (m)**	**Quantity**	**Remarks**
From	**To**								
E8		KSRB 2-1 : Earthwork in surface excavation for levelling and lowering the ground manually (Other than foundation of buildings, culverts, road drains and trenches of pipe lines and cables) and removing the excavated stuff to a distance not exceeding 50m and lift up to 1.5m, excavated surface levelled and neatly dressed, disposed earth to be levelled including breaking of clods and neatly dressed as per specifications. specification. No. KBS 2.1(a) / 2.3.1 KSRB 2-1.1: – do – Ordinary soil							
Measurement Taken on		7/1/23							
0	10								
10	20		Cum	1	10.00	4.30	0.65	27.95	
20	30.1		Cum	1	10.00	3.00	0.65	19.50	
			Cum	1	10.10	2.00	0.65	13.13	
		Total Executed Quantity						**60.58**	
		Quantity Carried to Summary						**60.58**	

A.E.E. (Project)

RUDRAPRASAD CONSULTANTS BANGALORE

CONTRACTOR PMC ASSISTANT ENGINEER ASSISTANT EXECUTIVE ENGINEER

Scanned by TapScanner

Scanned by TapScanner

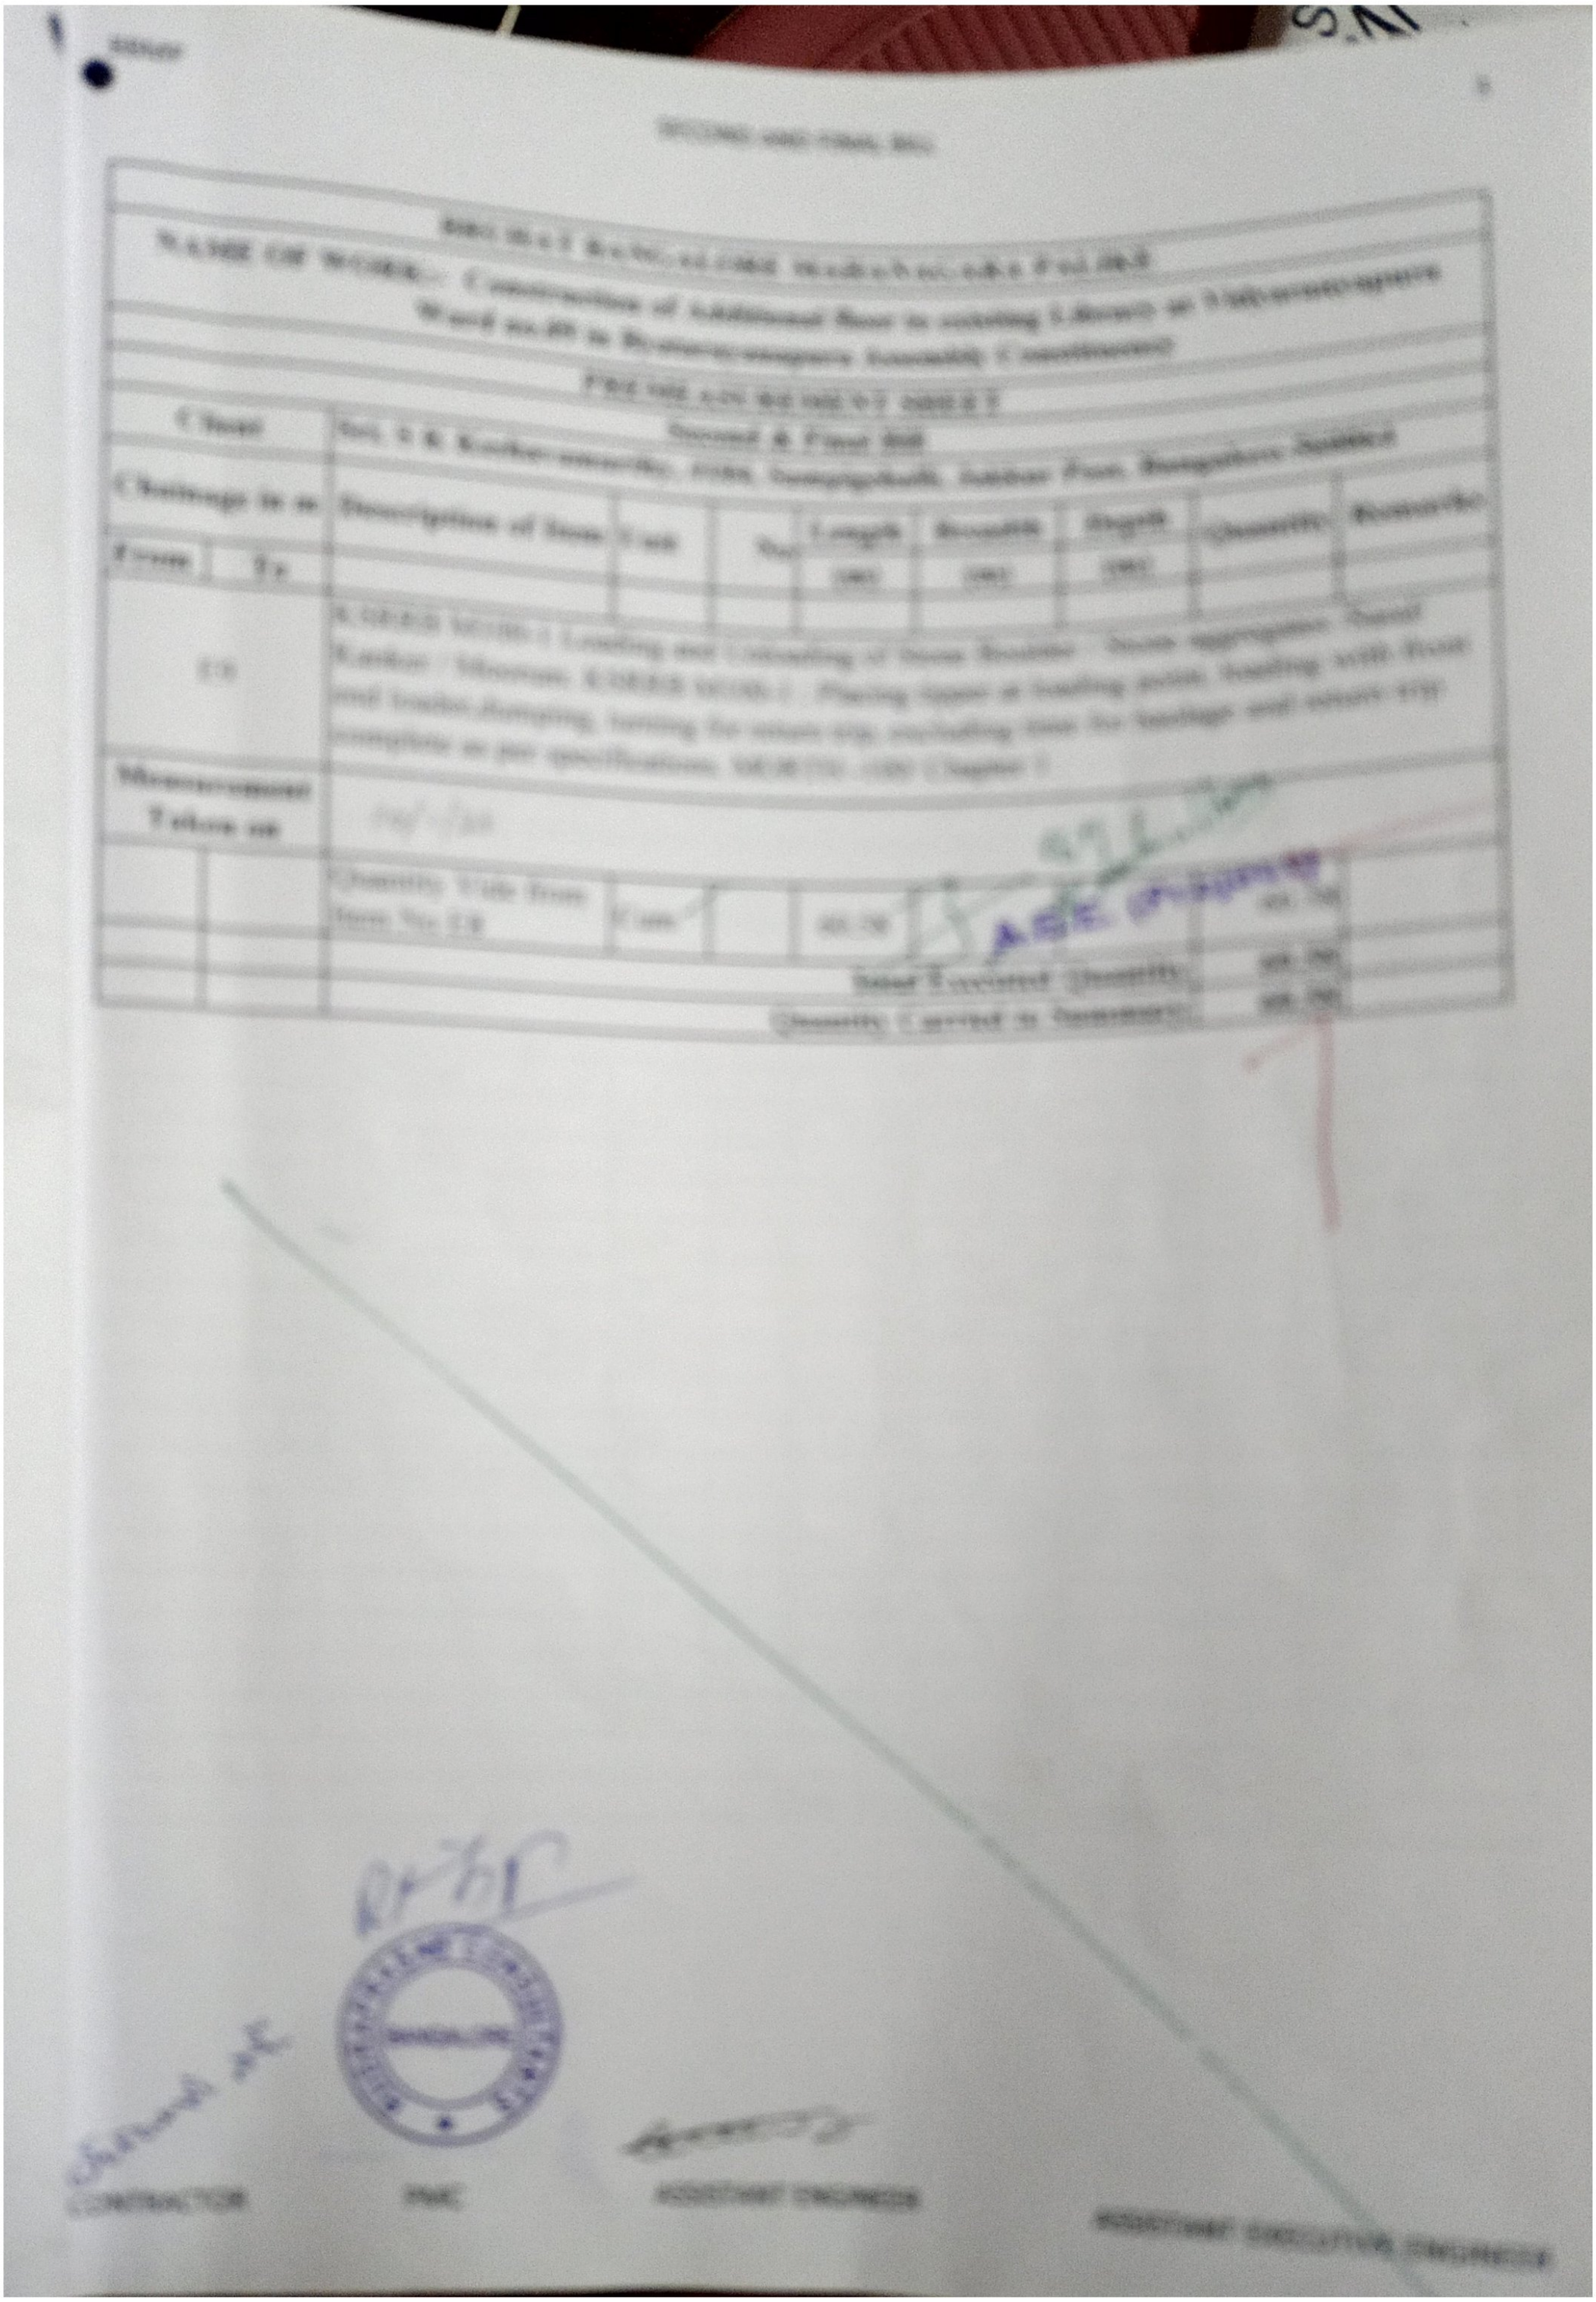

Scanned by TapScanner

Scanned by TapScanner

BRUHAT BANGALORE MAHANAGARA PALIKE									
NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency									
PREMEASUREMENT SHEET									
Client		Second & Final Bill							
		Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064							
Chainage in m		Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Remarks
From	To								
E10		KSRB 14.9-1: Providing and laying M-15 cement concrete flooring, 50 mm thick with metallic concrete hardner topping, under layer of 35mm thick m-15 cement concrete using broken granite metal of 20mm and down size, and top layer 50mm thick of metallic cement hardner consisting of mix 1:2 (1 cement hardner mix : 2 granite metal 10mm nominal size) by volume, with which metallic hardening compound of approved quality mix in the ratio of 4:1 (4 part of cement and 1 part of metallic floor hardening compound of approved quality by wt), including finishing cost of materials, labour, curing, complete as per specifications Specification No. KBS 14.4							
Measurement Taken on		18/2/23							
		2nd Floor							
		Hall	Sqm	1	24.50	14.50		355.25	
		Verandah	Sqm	1	7.94	4.62		36.68	
		1st Floor							
		Hall	Sqm	1	24.4	14.5		353.80	
		Verandah	Sqm	1	7.9	4.62		36.50	
		Beside verandah	Sqm	1	1.63	1		1.63	
		Beside Gents Toilet	Sqm	4	1.4	0.45		2.52	
		Deducation							
		Columns	Sqm	-12	0.485	0.24		-1.40	
		Ground Floor verandah							
			Sqm	1	4.45	4.98		22.16	
			Sqm	1	4.5	1.6		7.20	
			Sqm	1	1.5	0.4		0.60	
			Sqm	1	1.05	0.14		0.15	
			Sqm	1	4.7	0.32		1.50	
			Sqm	1	2.1	0.13		0.27	
		Total Executed Quantity						816.87	
		Quantity Carried to Summary						816.87	

CE, FE
R. Narayana 18/2/2023
A.E.E. (Project)

R.K.P.

RUDRAPRASAD CONSULTANTS BANGALORE

CONTRACTOR PMC ASSISTANT ENGINEER ASSISTANT EXECUTIVE ENGINEER

Scanned by TapScanner
Scanned by TapScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

MEASUREMENT SHEET

Second & Final Bill

Client — **Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064**

Chainage in m From	To	Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Rate Rs	Amount Rs	Remarks
Item No. 1		Dismantling burnt brick masonry in clay mortar/lime mortar/cement mortar and stacking the bricks within a radius of 50m and removing the debris to a distance upto 200m. As per the direction of the Engineer Incharge									
			Cum								
		Total Executed Quantity						**21.50**			
		Modified Schedule B Qty									
		Quantity upto 125%						**16.35**			
		Quantity above 125%						**5.15**			
		DPQ Quantity Paid in 1st RA Bill									
		Quantity upto 125%						**16.35**			
		Quantity above 125%						**5.15**			
		Now to be paid Quantity						**Nill**			
Item No. 2		Dismantling weather proof course and removing and conveying the debris to a distance upto 200m.As per the direction of the Engineer Incharge									
			Cum								
		Total Executed Quantity						**33.74**			
		Modified Schedule B Qty						**33.74**			
		DPQ Quantity Paid in 1st RA Bill						**33.74**			
		Now to be paid Quantity						**Nill**			
Item No. 3		Cost of Haulage Excluding Loading and Unloading MORTH -100/ Chapter 1 Case-1: Surface Road .As per the direction of the Engineer Incharge									
			t.km								
		Vide Total executed Quantity from premeasuremet Page no. 01						**148.26**			
		Tender Quantity						**100.54**			
		Quantity Upto 125%						**125.68**			
		Quantity Above 125%						**22.58**			
		DPQ Quantity Paid in 1st RA Bill						**70,72**			
		Now to be Paid Quantity									
		Quantity Upto 125%						**54.96**	**16.32**	**897.00**	
		Quantity Above 125%						**22.58**	**19.63**	**444.00**	
Item No. 4		Providing T.M.T. steel reinforcement for R.C.C. work including straightening, cutting, bending, hooking, placing in position, lapping and/or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks and wastage shall not be measured and paid) cost of materials, labour, HOM of machinery complete as per specifications.As per the direction of the Engineer Incharge									
			Tonne								
		Total Executed Quantity						**38.03**			
		Modified Schedule B Qty						**38.03**			
		DPQ Quantity Paid in 1st RA Bill						**38.03**			
		Now to be paid Quantity						**Nill**			
Item No. 5		Lift charges for steel of all diameters for additional floors over ground floor per floor height of 3.5 m. or part there of cost of labour, complete as per specifications. As per the direction of the Engineer Incharge									
			Tonne								
		Total Executed Quantity						**38.03**			
		Modified Schedule B Qty						**38.03**			
		DPQ Quantity Paid in 1st RA Bill						**38.03**			
		Now to be paid Quantity						**Nill**			

RUDRAPRASAD CONSULTANTS BANGALORE

CONTRACTOR PMC ASSISTANT ENGINEER ASSISTANT EXECUTIVE ENGINEER

30/04/202

A.E.E. (Project)

Scanned by TapScanner

Scanned by TapScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

MEASUREMENT SHEET

Second & Final Bill

Client		Sri. S.K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064									
Chainage in m		Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Rate Rs	Amount Rs	Remarks
From	To										
Item No. 6		Providing and removing Centering & Shuttering, strutting, propping etc., for columns, pillars, piers, abutments, post and struts, square/rectangular / polygon in plan including cost of all materials, labour complete as per specifications.As per the direction of the Engineer Incharge									
			Sqm								
		Total Executed Quantity						265.23			
		Modified Schedule B Qty						265.23			
		DPQ Quantity Paid in 1st RA Bill						265.23			
		Now to be paid Quantity						Nill			
Item No. 7		Providing and laying in position reinforced cement concrete of design mix M20 with OPC cement @320kgs, with 20mm and down size graded granite metal coarse aggregates @0.69cum and fine aggregates @0.46cum, with superplastisiser @3lts confirming to IS 9103-1999 reaffirmed-2008, machine mixed, concrete laid in layers not exceeding 15 cms thick, vibrated for RCC beams, columns, roof of all sizes in foundation plinth and superstructure ground floor level for roof slabs, staircase, lintles, columns, including cost of all materials, labour, HOM of machinery, curing, complete as per specifications. As per the direction of the Engineer Incharge									
Measurement Taken on		25/01/23 25/01/23									
		Quantity Measured in 1st RA Bill						18.71			
		Present Bill Measurements									
0	10		Cum	1	10.0	4.3	0.2	8.60			
10	20		Cum	1	10.0	3.0	0.2	6.00			
20	30.1		Cum	1	10.1	2.0	0.2	4.04			
		Total Executed Quantity						37.35			
		Modified Schedule B Qty						37.35			
		DPQ Quantity Paid in 1st RA Bill						18.71			
		Now to be paid Quantity						18.64	6487.59	120929.00	
Item No. 8		Providing and removing Centering & Shuttering, strutting, propping etc., and removal of form work for sides ands soffits of beams, beam haunchings, cantilever girders, bressumers and lintels not exceeding 1m in depth including cost of all materials, labour complete as per specifications.As per the direction of the Engineer Incharge									
			Sqm								
		Total Executed Quantity						466.35			
		Modified Schedule B Qty									
		Quantity upto 125%						466.35			
		DPQ Quantity Paid in 1st RA Bill									
		Quantity upto 125%						466.35			
		Now to be paid Quantity						Nill			
Item No. 9		Providing and removing Centering & Shuttering, strutting, propping etc., and removal of form work for flat surface such as suspended floors, roofs, landings, balconies and likes, thickness upto 200 mm including cost of all materials, labour complete as per specifications.As per the direction of the Engineer Incharge , 0 to 11mts									
			Sqm								
		Total Executed Quantity						1049.04			
		Modified Schedule B Qty									
		Quantity upto 125%						1049.04			
		DPQ Quantity Paid in 1st RA Bill									
		Quantity upto 125%						1049.04			
		Now to be paid Quantity						Nill			

A.E.E. (Project)

RUDRAPRASAD CONSULTANTS BANGALORE

CONTRACTOR PMC ASSISTANT ENGINEER ASSISTANT EXECUTIVE ENGINEER

A.E.E. (Project)

Scanned by TapScanner
Scanned by TapScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

MEASUREMENT SHEET

Second & Final Bill

Client		Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064									
Chainage in m		Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Rate Rs	Amount Rs	Remarks
From	To										
Item No. 10		Providing and constructing load bearing wall with solid concrete blocks having block density not less than 1800kg/m3 having a minimum average compressive strength of 4.00 N/mm2 confirming to IS 2185 (Part 1)2005 and constructed with CM 1 A, as per IS 25722005 including cost of all materials labour charges, scaffolding, curing, hire charges of machineries etc., complete as per specifications. As per the direction of the Engineer Incharge									
			Sqm								
		Total Executed Quantity						595.22			
		Modified Schedule B Qty						595.22			
		DPQ Quantity Paid in 1st RA Bill						595.22			
		Now to be paid Quantity						Nill			
Item No. 11		Providing and constructing load bearing wall with solid concrete blocks having block density not less than 1800kg/m3 having a minimum average compressive strength of 4.00 N/mm2 confirming to IS 2185 (Part 1)2005 and constructed with CM 1 A, as per IS 25722005 including cost of all materials labour charges, scaffolding, curing, hire charges of machineries etc., complete as per specifications. As per the direction of the Engineer Incharge									
Measurement Taken on		11/01/23 11/01/23									
		Quantity Measured in 1st RA Bill						22.87			
		Present Bill Measurements									
		2nd Floor Near Lift Walls	Sqm	1	1.50		1.60	2.40			
		1st Floor Near Lift Walls	Sqm	1	1.50		1.60	2.40			
		Terrace Walls	Sqm	1	3.34		1.60	5.34			
			Sqm	1	1.10		2.30	2.53			
		Ground Floor Near Lift	Sqm	1	1.47		1.60	2.35			
		1st Floor Near Verandha	Sqm	2	1.55		1.12	3.47			
		2nd Floor Near Verandha	Sqm	2	1.55		1.12	3.47			
		1st Floor									
		Gents Toilet									
		Long Wall Side	Sqm	1	3.77		3.05	11.50			
			Sqm	1	1.02		3.15	3.21			
			Sqm	1	0.63		3.05	1.92			
		Short Wall Side	Sqm	1	1.21		3.05	3.69			
			Sqm	1	1.17		3.05	3.57			
			Sqm	1	1.46		3.05	4.45			
		Ladies Toilet									
		Long Wall Side	Sqm	1	0.44		3.05	1.34			
			Sqm	1	0.45		3.05	1.37			
		Short Wall Side	Sqm	1	1.29		3.05	3.93			
			Sqm	1	1.27		3.05	3.87			
			Sqm	1	1.18		3.05	3.60			
			Sqm	1	1.30		3.05	3.97			
		2nd Floor									
		Gents Toilet									
		Long Wall Side	Sqm	1	3.83		3.05	11.68			
			Sqm	1	1.10		3.15	3.47			
			Sqm	1	0.60		3.05	1.83			
		Short Wall Side	Sqm	1	1.50		3.05	4.58			
			Sqm	1	1.16		3.05	3.54			
			Sqm	1	1.45		3.05	4.42			
		Ladies Toilet									
		Long Wall Side	Sqm	1	0.44		3.05	1.34			
			Sqm	1	0.45		3.05	1.37			
		Short Wall Side	Sqm	1	1.29		3.05	3.93			
			Sqm	1	1.27		3.05	3.87			
			Sqm	1	1.18		3.05	3.60			

Executive Engineer Project Division Yelahanka Zone BBMP, Bangalore-92

C&FC 30/04/2023

A.E.E. (Project)

112.04

RUDRAPRASAD CONSULTANTS BANGALORE

CONTRACTOR PMC ASSISTANT ENGINEER ASSISTANT EXECUTIVE ENGINEER

Scanned by TapScanner

Scanned by TapScanner

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

BRUHAT BANGALORE MAHANAGARA PALIKE

MEASUREMENT SHEET

Second & Final Bill

Client | **Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064**

Chainage in m From	To	Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Rate Rs	Amount Rs	Remarks
		Deducation	Sqm	1	1.30		3.05	3.97			
		Terrace Walls Columns	Sqm	-2	0.17		1.60	-0.54			
							Total Executed Quantity	**138.33**			
							Modified Schedule B Qty	**138.33**			
							DPQ Quantity Paid in 1st RA Bill	**22.87**			
							Now to be Paid Quantity	**115.46**	**1074.88**	**124101.00**	
Item No. 12		Providing and laying in position reinforced cement concrete of design mix M20 with OPC cement @320kgs, with 20mm and down size graded granite metal coarse aggregates @0.878cum and fine aggregates @0.459cum, with superplastisiser @3lts confirming to IS 9103-1999 reaffirmed-2008, machine mixed, concrete laid in layers not exceeding 15 cms thick, vibrated for all works in foundation plinth and ground floor level for roof slabs, staircase, lintles, retaining walls, return walls, walls (any thickness) including attached pilasters, columns, piers, abutments, pillars, posts, struts, buttresses, string or lacing courses, parapets, coping, bed blocks, anchor blocks, plain window cills, fillets etc., including cost of all materials, labour, HOM of machinery, curing, complete as per specifications.As per the direction of the Engineer Incharge									
			Cum								
							Total Executed Quantity	**231.74**			
							Modified Schedule B Qty	**231.74**			
							Quantity upto 125%	**231.74**			
							DPQ Quantity Paid in 1st RA Bill				
							Quantity upto 125%	**231.74**			
							Now to be paid Quantity	**Nill**			
Item No. 13		Providing 18mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners wherever required smooth rendering, Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications.As per the direction of the Engineer Incharge (Inside Plastering)									
Measurement Taken on		19/1/23			19/1/23						
		Quantity Measured in 1st RA Bill						**900.57**			
		Present Bill Measurements									
		2nd Floor Near Lift Walls	Sqm	2	1.50		1.60	4.80			
		1st Floor Near Lift Walls	Sqm	2	1.50		1.60	4.80			
		Terrace Walls	Sqm	2	3.34		1.60	10.69			
			Sqm	2	1.10		2.30	5.06			
		Ground Floor Near Lift	Sqm	2	1.47		1.60	4.70			
		1st Floor Near Verandha	Sqm	4	1.55		1.12	6.94			
			Sqm	2	1.55	0.10		0.31			
			Sqm	2	1.12	0.10		0.22			
		2nd Floor Near Verandha	Sqm	4	1.55		1.12	6.94			
			Sqm	2	1.55	0.10		0.31			
			Sqm	2	1.12	0.10		0.22			
		1st Floor									
		Gents Toilet									
		Long Wall Side	Sqm	2	3.77		1.09	8.22			
			Sqm	2	1.02		1.19	2.43			
			Sqm	2	0.63		1.09	1.37			
		Short Wall Side	Sqm	2	1.21		1.09	2.64			
			Sqm	2	1.17		1.09	2.55			
			Sqm	2	1.46		1.09	3.18			
		Ladies Toilet									
		Long Wall Side	Sqm	2	0.44		0.95	0.84			
			Sqm	2	0.45		0.95	0.86			
		Short Wall Side	Sqm	2	1.29		0.95	2.45			
			Sqm	2	1.27		0.95	2.41			

CONTRACTOR

RUDRAPRASAD CONSULTANTS BANGALORE

PMC

ASSISTANT ENGINEER

C&FC

A.E.E. (Project) 30/09/2023

ASSISTANT EXECUTIVE ENGINEER

Scanned by TapScanner

Scanned by TapScanner

BMP

SECOND AND FINAL BILL

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

MEASUREMENT SHEET

Second & Final Bill

Client | **Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064**

Chainage in m From	To	Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Rate Rs	Amount Rs	Remarks
			Sqm	2	1.18		0.95	2.24			
			Sqm	2	1.30		0.95	2.47			
		2nd Floor									
		Gents Toilet									
		Long Wall Side									
			Sqm	2	3.83		1.09	8.35			
			Sqm	2	1.10		1.19	2.62			
		Short Wall Side	Sqm	2	0.60		1.09	1.31			
			Sqm	2	1.50		1.09	3.27			
			Sqm	2	1.16		1.09	2.53			
			Sqm	2	1.45		1.09	3.16			
		Ladies Toilet									
		Long Wall Side									
			Sqm	2	0.44		0.95	0.84			
			Sqm	2	0.45		0.95	0.86			
		Short Wall Side	Sqm	2	1.29		0.95	2.45			
			Sqm	2	1.27		0.95	2.41			
			Sqm	2	1.18		0.95	2.24			
			Sqm	2	1.30		0.95	2.47			
							Total Executed Quantity	**1009.74**			
							Modified Schedule B Qty	**1009.74**			
							DPQ Quantity Paid in 1st RA Bill	**900.57**			
							Now to be Paid Quantity	**109.17**	**247.13**	**26978.00**	

Item No. 14		Providing 20mm thick cement plaster in single coat with cement mortar 1:4, to stone masonry & concrete surface including rounding off corners wherever required smooth rendering, Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications As per the direction of the Engineer Incharge (External plastering)									
			Sqm								
							Total Executed Quantity	**832.21**			
							Modified Schedule B Qty	**832.21**			
							DPQ Quantity Paid in 1st RA Bill	**832.21**			
							Now to be paid Quantity	**Nill**			
Item No. 15		Providing 12mm thick cement plaster in single coat with cement mortar 1:4 to Ceiling including rounding off corners wherever required smooth rendering, Provinding and removing scaffolding, including cost of materials, labour, curing complete as per specifications. As per the direction of the Engineer Incharge (Ceiling plaster)									
			Sqm								
							Total Executed Quantity	**1020.97**			
							Modified Schedule B Qty				
							Quantity upto 125%	**967.16**			
							Quantity above 125%	**53.81**			
							DPQ Quantity Paid in 1st RA Bill				
							Quantity upto 125%	**967.16**			
							Quantity above 125%	**53.81**			
							Now to be paid Quantity	**Nill**			
Item No.16		Providing and finishing external walls in two coats with Water Proof Cement paint of approved brand and shade to give an even shade after throughly brooming the surface to remove all dirt and loose powdered material, free from mortar drops and other foreign matter cost of materials, labour, complete as per specifications As per the direction of the Engineer Incharge									
Measurement Taken on		15/2/23			15/2/23						
		For First floor									
		Longer span	Sqm	1	29.35		3.35	98.32			
			Sqm	1	24.30		3.35	81.41			
		Shorter span	Sqm	1	15.00		3.35	50.25			
			Sqm	1	5.00		3.35	16.75			
		Parapet walls	Sqm	1	0.93		0.90	0.84			

247.56 C & FC 30/09/2023

A.E.E. (Project)

RUDRAPRASAD CONSULTANTS BANGALORE

NTRACTOR PMC ASSISTANT ENGINEER ASSISTANT EXECUTIVE ENGINEER

Scanned by TapScanner

Scanned by TapScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

MEASUREMENT SHEET

Second & Final Bill

Client: Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064

Chainage in m From	Chainage in m To	Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Rate Rs	Amount Rs	Remarks
			Sqm	1	6.40		0.90	5.76			
			Sqm	1	1.44		0.93	1.34			
			Sqm	1	4.79		0.96	4.60			
		Chejja									
		Top and bottom	Sqm	19	4.50	0.40		34.20			
		Sides	Sqm	19	3.05	0.08		4.35			
		Deductions									
		W	Sqm	-9.5	1.85		1.50	-26.36			
		Out Side Columns									
			Sqm	6	0.45		3.15	8.51			
			Sqm	6	0.45		3.15	8.51			
		Slab Projected Outside	Sqm	2	24.30	0.45		21.87			
		Slab Side Face	Sqm	2	24.30		0.20	9.72			
			Sqm	4	0.45	0.20		0.36			
		For Second floor									
		Longer span	Sqm	1	29.35		3.35	98.32			
			Sqm	1	24.3		3.35	81.41			
		Shorter span	Sqm	1	15		3.35	50.25			
			Sqm	1	5		3.35	16.75			
		Parapet walls	Sqm	1	0.93		0.9	0.84			
			Sqm	1	6.4		0.9	5.76			
			Sqm	1	1.44		0.93	1.34			
			Sqm	1	4.79		0.96	4.60			
		Chejja									
		Top and bottom	Sqm	19	4.50	0.4		34.20			
		Sides	Sqm	19	3.05	0.075		4.35			
		Deductions									
		W	Sqm	-9.5	1.85		1.5	-26.36			
		Out Side Columns									
			Sqm	6	0.45		3.15	8.51			
			Sqm	6	0.45		3.15	8.51			
		Slab Projected Outside	Sqm	2	24.3	0.45		21.87			
		Slab Side Face	Sqm	2	24.3		0.2	9.72			
			Sqm	4	0.45	0.2		0.36			
		Head Room	Sqm	1	5.07		3.00	15.21			
			Sqm	2	5.67		3.00	34.02			
		Side Face	Sqm	2	5.67	0.20		2.27			
		Parapet walls	Sqm	2	29.35		1.04	61.05			
			Sqm	2	24.30		1.04	50.54			
			Sqm	2	4.98		1.04	10.36			
			Sqm	2	15.45		1.04	32.14			
			Sqm	2	0.79		1.04	1.64			
			Sqm	2	6.40		1.04	13.31			
			Sqm	2	3.00		1.04	6.24			
		Top Face	Sqm	1	29.35	0.15		4.40			
			Sqm	1	24.3	0.15		3.65			
			Sqm	1	4.98	0.15		0.75			
			Sqm	1	15.45	0.15		2.32			
			Sqm	1	0.79	0.15		0.12			
			Sqm	1	6.4	0.15		0.96			
			Sqm	1	3	0.15		0.45			
		Ground Floor Out Side									
		Longer span	Sqm	2	24.8		3.35	166.16			
			Sqm	1	4.85		3.35	16.25			

1062.64

C & FC 30/04/2023

RUDRAPRASAD CONSULTANTS BANGALORE PMC

CONTRACTOR | ASSISTANT ENGINEER | ASSISTANT EXECUTIVE ENGINEER

Asst. Executive Engineer Project Division Yelahanka Zone BBMP, Bengaluru - 92

Scanned by TapScanner

Scanned by TapScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

MEASUREMENT SHEET

Second & Final Bill

Client: Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064

Rs 1062.64

Chainage in m From	To	Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Rate Rs	Amount Rs	Remarks
		Shorter span	Sqm	1	15.85		3.6	57.06			
			Sqm	1	5.25		3.35	17.59			
		Deductions	Sqm	1	5.05		3.35	16.92			
		W	Sqm								
		W1	Sqm	-19	1.8		1.2	-41.04			
		M.D	Sqm	-1	1		1	-1.00			
		Out Side Columns	Sqm	-2	1.4		1.97	-5.52			
		Compound Wall	Sqm	8	0.9		3.15	22.68			
			Sqm	1	10.1		1.1	11.11			
			Sqm	1	10.1	0.16		1.62			
			Sqm	2	41.3		1.22	100.77			
		Columns	Sqm	1	41.3	0.18		7.43			
			Sqm	7	0.6		1.7	7.14			
			Sqm	7	0.1		1.7	1.19			
			Sqm	6	0.78		2.1	9.83			
		Deductions									
		Gate	Sqm	-2	3.1		1.22	-7.56			
		Gate	Sqm	-1	1.9		1.22	-2.32			
		Senior citizen Building									
		Ground Floor									
		North Side									
		Wall	Sqm	1	8.9		3.75	33.38			
		Beams	Sqm	3	0.6		1.3	2.34			
			Sqm	3	1.3	0.25		0.98			
		Slab	Sqm	1	8.15	1.3		10.60			
			Sqm	1	1.75	1.3		2.28			
		Deduction									
		Door	Sqm	-1	1.5		2.1	-3.15			
		Window	Sqm	-1	1.45		1.8	-2.61			
		Name Board	Sqm	-1	0.6		1.53	-0.92			
		South Side									
		Wall	Sqm	1	8.9		3.9	34.71			
		Chejja									
		For Window	Sqm	4	1.56	0.45		2.81			
			Sqm	4	0.45		0.1	0.18			
		For Ventilator	Sqm	2	1	0.4		0.80			
			Sqm	2	0.4		0.1	0.08			
		Deduction									
		Window	Sqm	-2	1.2		1.46	-3.50			
		Ventilator	Sqm	-1	0.6		0.6	-0.36			
		East Side									
		Wall	Sqm	1	17.46		3.75	65.48			
		Slab projection									
		Top Face	Sqm	1	17.46	0.45		7.86			
		Bottom Face	Sqm	1	17.46	0.37		6.46			
		Side Face	Sqm	1	17.46		0.15	2.62			
		Beam	Sqm	1	17.46	0.09		1.57			
			Sqm	1	17.46		0.3	5.24			
		Column	Sqm	6	0.34		3.9	7.96			
			Sqm	10	0.45		3.75	16.88			
		Chejja									
		Size 2.2X0.45	Sqm	8	2.2	0.45		7.92			
			Sqm	8	0.45		0.1	0.36			

1458.46

C & FC 30/04/2023

RUDRAPRASAD CONSULTANTS BANGALORE

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

CONTRACTOR PMC ASSISTANT ENGINEER ASSISTANT EXECUTIVE ENGINEER

Scanned by TapScanner

Scanned by TapScanner

BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

MEASUREMENT SHEET

Second & Final Bill

1458.46

Client	Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064									
Chainage in m	Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Rate Rs	Amount Rs	Remarks
From / To										
	Size 1.56X0.45	Sqm	2	1.56	0.45		1.40			
		Sqm	2	0.45		0.1	0.09			
	Plinth Beam	Sqm	1	17.46		0.3	5.24			
		Sqm	1	17.46	0.09		1.57			
	Deduction									
	Window	Sqm	-4	1.45		1.8	-10.44			
		Sqm	-1	1.2		1.46	-1.75			
						Total Executed Quantity	1454.58			
						Modified Schedule B Qty	1454.58			
						Now to be Paid Quantity	1454.58	119.34	173590.00	

Item No. 17	Providing and applying two coats with oil bound washable distermper Two Coats of distemper of approved brand and shade on Ceilling & sloped roof including priming coat with distemper primer after throughly brooming the surface free from mortar drops and other foreign matter including preparing the surface even and sand paper smooth, cost of materials, labour, complete as per specifications..As per the direction of the Engineer Incharge
Measurement Taken on	15/2/23 15/2/23

First Floor							
Hall	Sqm	2	24.23		3.06	148.29	
	Sqm	2	14.60		3.06	89.35	
Deduction							
W	Sqm	-19	1.80		1.50	-51.30	
MD	Sqm	-1	1.44		1.97	-2.84	
Door Near Toilet	Sqm	-3	0.92		1.93	-5.33	
Celing	Sqm	1	24.23	14.50		351.34	
Beams	Sqm	4	24.23		0.45	43.61	
	Sqm	6	14.60		0.46	40.30	
Columns (6nos)	Sqm	12	0.48		2.53	14.57	
	Sqm	12	0.46		2.53	13.97	
Window Portion	Sqm	19	1.80	0.12		4.10	
	Sqm	19		1.50	0.12	3.42	
Gents Toilet	Sqm	1	1.02		1.06	1.08	
	Sqm	2	1.17		1.06	2.48	
	Sqm	1	2.12		1.06	2.25	
	Sqm	1	1.44		1.06	1.53	
	Sqm	1	0.80		1.06	0.85	
	Sqm	1	0.63		1.06	0.67	
	Sqm	1	1.28		1.06	1.36	
	Sqm	1	1.35		1.06	1.43	
	Sqm	1	2.40		1.06	2.54	
	Sqm	1	4.55		1.06	4.82	
	Sqm	1	1.46		1.06	1.55	
Deduction							
V	Sqm	1	1.30		0.43	0.56	
V1	Sqm	1	0.65		0.45	0.29	
Celing	Sqm	1	4.55	2.40		10.92	
Deduction	Sqm	-1	1.44	0.13		-0.19	
	Sqm	-1	0.63	0.13		-0.08	
	Sqm	-1	1.17	0.13		-0.15	
Ladies Toilet	Sqm	1	1.06		1.10	1.17	
	Sqm	2	1.18		1.10	2.60	
	Sqm	1	1.00		1.10	1.10	
	Sqm	1	1.37		1.10	1.51	
	Sqm	2	1.15		1.10	2.53	

690.29

CE & FC Navleen 3/4/2023

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

RUDRAPRASAD CONSULTANTS BANGALORE

CONTRACTOR PMC ASSISTANT ENGINEER ASSISTANT EXECUTIVE ENGINEER

Scanned by TapScanner

Scanned by TapScanner

BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

MEASUREMENT SHEET

Second & Final Bill

Client		Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064									
Chainage in m		Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Rate Rs	Amount Rs	Remarks
From	To										
			Sqm	4	1.37		1.10	6.03			
			Sqm	2	1.17		1.10	2.57			
			Sqm	1	0.85		1.10	0.94			
			Sqm	1	4.65		1.10	5.12			
			Sqm	1	1.30		1.10	1.43			
		Deduction									
		D	Sqm	-1	0.73		2.00	-1.46			
		D1	Sqm	-1	0.70		2.00	-1.40			
		V	Sqm	-1	0.63		0.42	-0.26			
		V1	Sqm	-1	1.25		0.42	-0.53			
		V2	Sqm	-1	0.60		0.60	-0.36			
		Celing	Sqm	1	2.22	4.62		10.26			
		Beams	Sqm	2	4.62	0.46		4.25			
		Deduction	Sqm	-1	1.17	0.13		-0.15			
			Sqm	-1	1.15	0.13		-0.15			
			Sqm	-2	1.37	0.13		-0.36			
			Sqm	-1	1.18	0.13		-0.15			
		Verandha									
		Celing	Sqm	1	8.13	4.86		39.51			
		Parapet walls	Sqm	1	0.93		0.90	0.84			
			Sqm	1	6.40		0.90	5.76			
			Sqm	1	1.44		0.93	1.34			
			Sqm	1	4.79		0.96	4.60			
		On top Face	Sqm	1	0.93	0.13		0.12			
			Sqm	1	6.4	0.13		0.83			
			Sqm	1	1.44	0.13		0.19			
			Sqm	1	4.79	0.13		0.62			
		Side Face	Sqm	2	0.90	0.13		0.23			
		Column	Sqm	2	0.48		3.05	2.93			
			Sqm	2	0.23		3.05	1.40			
		Beams	Sqm	2	8.13		0.46	7.48			
			Sqm	4	4.86		0.46	8.94			
		Stair case bottom									
		1st flight	Sqm	1.00	2.40	1.37		3.29			
		Landing	Sqm	1.00	1.53	1.37		2.10			
		2nd flight	Sqm	1.00	1.80	1.37		2.47			
		Landing	Sqm	1.00	1.50	1.35		2.03			
		3rd flight	Sqm	1.00	1.50	1.37		2.06			
		Lift Walls	Sqm	2.00	1.84		1.60	5.89			
			Sqm	2.00	1.84		2.40	8.83			
			Sqm	4.00	2.20		2.40	21.12			
		Stiar Case Area									
			Sqm	1.00	4.60		2.40	11.04			
			Sqm	1.00	3.60		2.40	8.64			
		Deducation									
		W	Sqm	-1.00	1.00		1.00	-1.00			
		Stair Case Waist Slab									
		1st flight	Sqm	-2.00	2.40	0.175		-0.84			
		Landing	Sqm	-2.00	1.53	0.175		-0.54			
		2nd flight	Sqm	-2.00	1.80	0.175		-0.63			
		Landing	Sqm	-2.00	1.53	0.175		-0.54			
		3rd flight	Sqm	-2.00	1.50	0.175		-0.53			
		Second Floor									
		Hall	Sqm	2	24.23		3.06	148.29			

690.29

1002.52

CC FC
K. Nanker 30/09/2023

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

RUDRAPRASAD CONSULTANTS BANGALORE

CONTRACTOR

PMC

ASSISTANT ENGINEER

ASSISTANT EXECUTIVE ENGINEER

Scanned by TapScanner

Scanned by TapScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

MEASUREMENT SHEET

Second & Final Bill

1002.52

Client		Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064									
Chainage in m		Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Rate Rs	Amount Rs	Remarks
From	To										
		Deduction	Sqm	2	14.60		3.06	89.35			
		W									
		MD	Sqm	-19	1.80		1.50	-51.30			
		Door Near Toilet	Sqm	-1	1.44		1.97	-2.84			
		Celing	Sqm	-3	0.92		1.93	-5.33			
		Beams	Sqm	1	24.23	14.50		351.34			
			Sqm	4	24.23		0.45	43.61			
		Columns (6nos)	Sqm	6	14.60		0.46	40.30			
			Sqm	12	0.48		2.53	14.57			
			Sqm	12	0.46		2.53	13.97			
		Window Portion	Sqm	19	1.80	0.12		4.10			
			Sqm	19		1.50	0.12	3.42			
		Gents Toilet	Sqm	1	1.02		1.06	1.08			
			Sqm	2	1.17		1.06	2.48			
			Sqm	1	2.12		1.06	2.25			
			Sqm	1	1.44		1.06	1.53			
			Sqm	1	0.80		1.06	0.85			
			Sqm	1	0.63		1.06	0.67			
			Sqm	1	1.28		1.06	1.36			
			Sqm	1	1.35		1.06	1.43			
			Sqm	1	2.40		1.06	2.54			
			Sqm	1	4.55		1.06	4.82			
			Sqm	1	1.46		1.06	1.55			
		Deduction									
		V	Sqm	1	1.30		0.43	0.56			
		V1	Sqm	-1	0.65		0.45	0.29			
		Celing	Sqm	1	4.55	2.40		10.92			
		Deduction	Sqm	-1	1.44	0.13		-0.19			
			Sqm	-1	0.63	0.13		-0.08			
			Sqm	-1	1.17	0.13		-0.15			
		Ladies Toilet	Sqm	1	1.06		1.10	1.17			
			Sqm	2	1.18		1.10	2.60			
			Sqm	1	1.00		1.10	1.10			
			Sqm	1	1.37		1.10	1.51			
			Sqm	2	1.15		1.10	2.53			
			Sqm	4	1.37		1.10	6.03			
			Sqm	2	1.17		1.10	2.57			
			Sqm	1	0.85		1.10	0.94			
			Sqm	1	4.65		1.10	5.12			
			Sqm	1	1.30		1.10	1.43			
		Deduction	Sqm	-1	0.73		2.00	-1.46			
		D	Sqm	-1	0.70		2.00	-1.40			
		D1	Sqm	-1	0.63		0.42	-0.26			
		V	Sqm	-1	1.25		0.42	-0.53			
		V1	Sqm	-1	0.60		0.60	-0.36			
		V2	Sqm	1	2.22	4.62		10.26			
		Celing	Sqm	2	4.62	0.46		4.25			
		Beams	Sqm	-1	1.17	0.13		-0.15			
		Deduction	Sqm	-1	1.15	0.13		-0.15			
			Sqm	-2	1.37	0.13		-0.36			
			Sqm	-1	1.18	0.13		-0.15			
		Verandha	Sqm	1	8.13	4.86		39.51			
		Celing									

1609.80

CE FC 30/04/2023

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

RUDRAPRASAD CONSULTANTS BANGALORE

CONTRACTOR | PMC | ASSISTANT ENGINEER | ASSISTANT EXECUTIVE ENGINEER

Scanned by TapScanner
Scanned by TapScanner

SECOND AND FINAL BILL

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

MEASUREMENT SHEET

Second & Final Bill

Client: **Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064**

Chainage in m From	To	Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Rate Rs	Amount Rs	Remarks
		Parapet walls									
			Sqm	1	0.93		0.90	0.84			
			Sqm	1	6.40		0.90	5.76			
			Sqm	1	1.44		0.93	1.34			
			Sqm	1	4.79		0.96	4.60			
		On top Face	Sqm	1	0.93	0.13		0.12			
			Sqm	1	6.40	0.13		0.83			
			Sqm	1	1.44	0.13		0.19			
			Sqm	1	4.79	0.13		0.62			
		Side Face	Sqm	2	0.90	0.13		0.23			
		Column	Sqm	2	0.48		3.05	2.93			
			Sqm	2	0.23		3.05	1.40			
		Beams	Sqm	2	8.13		0.46	7.48			
			Sqm	4	4.86		0.46	8.94			
		Stair case bottom									
		1st flight	Sqm	1	2.40	1.37		3.29			
		Landing	Sqm	1	1.53	1.37		2.10			
		2nd flight	Sqm	1	1.80	1.37		2.47			
		Landing	Sqm	1	1.50	1.35		2.03			
		3rd flight	Sqm	1	1.50	1.37		2.06			
		Lift Walls	Sqm	2	1.84		1.60	5.89			
			Sqm	2	1.84		2.40	8.83			
			Sqm	4	2.20		2.40	21.12			
		Stiar Case Area									
			Sqm	1	4.60		2.40	11.04			
			Sqm	1	3.60		2.40	8.64			
		Deducation									
		W	Sqm	-1	1.00		1.00	-1.00			
		Stair Case Waist Slab									
		1st flight	Sqm	-2	2.40	0.175		-0.84			
		Landing	Sqm	-2	1.53	0.175		-0.54			
		2nd flight	Sqm	-2	1.80	0.175		-0.63			
		Landing	Sqm	-2	1.53	0.175		-0.54			
		3rd flight	Sqm	-2	1.50	0.175		-0.53			
		Head Room									
		Lift Walls	Sqm	2	3.34		1.60	10.69			
			Sqm	2	1.84		2.40	8.83			
			Sqm	4	2.20		2.40	21.12			
		Head Room walls	Sqm	1	5.07		3.00	15.21			
			Sqm	2	5.67		3.00	34.02			
		Ground Floor									
		Verandha									
		Wall	Sqm	1	12.55		3.05	38.28			
		Celing	Sqm	1	7.20		4.86	34.99			
		Columns (2nos)	Sqm	2	1.80		3.05	10.98			
		Lift Walls	Sqm	2	1.84		1.60	5.89			
			Sqm	2	1.84		2.40	8.83			
			Sqm	4	2.20		2.40	21.12			
		Stiar Case Area									
			Sqm	1	4.60		2.40	11.04			
			Sqm	1	3.60		2.40	8.64			

1938.11

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

RUDRAPRASAD CONSULTANTS BANGALORE

CONTRACTOR | PMC | ASSISTANT ENGINEER | ASSISTANT EXECUTIVE ENGINEER

Scanned by TapScanner

Scanned by TapScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

MEASUREMENT SHEET

Second & Final Bill

Client		Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064									
Chainage in m		Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Rate Rs	Amount Rs	Remarks
From	To										
		Deducation									
		W	Sqm	-1	1.00		1.00	-1.00			
		Total Executed Quantity						1937.11			
		Modified Schedule B Qty						1937.11			
		Now to be Paid Quantity						1937.11	119.99	232434.00	
Item No.18		Providing and fixing Vitrified blessed tiles of approved make, quality and colour of size 600 x 600 x 10 mm thick fixed on bed of 12 thick cement mortar for flooring, Skirting and jointed with neat cement slurry mixed with figment to mach shade of tiles, including providing spacers required intervals and removing stains etc. complete as per specification.As per the direction of the Engineer Incharge									
		Item Not Operated									
Item No.19		Providing Ceramic tiles of approved make,shade and size for flooring, treads of steps and landings laid on a bed of 12mm thick, cement mortar 1:3 mix, flush pointing with white cement using colour pigment , including cost of materials, labour, curing, complete as per specifications. - for Ceramic tiles 30cm x 60cm 6mm thick on a bed of 20mm thick. As per the direction of the Engineer Incharge									
Measurement Taken on		30/1/23 30/1/23									
		Floor Tiles									
		2nd Floor Toilet Room									
		Gents Toilet									
			Sqm	1	0.92	0.22		0.20			
			Sqm	1	1.14	0.85		0.97			
			Sqm	1	1.20	1.04		1.25			
			Sqm	1	2.40	2.15		5.16			
			Sqm	1	1.50	0.85		1.28			
			Sqm	1	0.72	0.16		0.12			
			Sqm	1	1.35	1.30		1.76			
		Ladies Toilet									
			Sqm	1	0.90	0.18		0.16			
			Sqm	1	2.23	0.88		1.96			
			Sqm	1	1.20	1.06		1.27			
			Sqm	1	2.65	0.85		2.25			
			Sqm	1	1.15	1.00		1.15			
			Sqm	1	1.22	1.15		1.40			
			Sqm	1	1.23	1.20		1.48			
		1st Floor Toilet Room									
		Gents Toilet									
			Sqm	1	0.92	0.22		0.20			
			Sqm	1	1.14	0.85		0.97			
			Sqm	1	1.20	1.04		1.25			
			Sqm	1	2.40	2.15		5.16			
			Sqm	1	1.50	0.85		1.28			
			Sqm	1	0.72	0.16		0.12			
			Sqm	1	1.35	1.30		1.76			
		Ladies Toilet									
			Sqm	1	0.90	0.18		0.16			
			Sqm	1	2.23	0.88		1.96			
			Sqm	1	1.20	1.06		1.27			
			Sqm	1	2.65	0.85		2.25			
			Sqm	1	1.15	1.00		1.15			

CF 1938.11

37.93

C&FC 30/09/2023

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

RUDRAPRASAD CONSULTANTS BANGALORE

CONTRACTOR PMC ASSISTANT ENGINEER ASSISTANT EXECUTIVE ENGINEER

Scanned by TapScanner

Scanned by TapScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

MEASUREMENT SHEET

Second & Final Bill

Client		Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064									
Chainage in m		Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Rate Rs	Amount Rs	Remarks
From	To										
			Sqm	1	1.22	1.15		1.40			
			Sqm	1	1.23	1.20		1.48			
		Total Executed Quantity						40.81			
		Tender Quantity						21.10			
		Quantity Upto 125%						26.38			
		Quantity Above 125%						14.43			
		Now to be Paid Quantity									
		Quantity Upto 125%						26.38	1045.92	27587.00	
		Quantity Above 125%						14.43	1386.41	20006.00	
Item No.20		Providing skirting, dado, rises of steps with colour glazed tiles on 10mm thick cement plaster 1:3 and jointed with white cement slurry over rough plaster surface (excluding cost of rough plastered surface which should be measured and paid separately) using glazed tiles of approved make and size including cost of materials, labour, complete as per specifications. - Colour glazed tiles 15x15 cms 6mm thick.As per the direction of the Engineer Incharge									
Measurement Taken on		30/1/23 30/1/23									
		Wall Cladding									
		2nd Floor Toilet									
		Gents Toilet									
			Sqm	1	15.00		1.96	29.40			
			Sqm	1	4.90		1.96	9.60			
		Ladies Toilet									
			Sqm	1	15.00		2.10	31.50			
			Sqm	1	8.20		2.10	17.22			
		1st Floor Toilet									
		Gents Toilet									
			Sqm	1	15.00		1.96	29.40			
			Sqm	1	4.80		1.96	9.41			
		Ladies Toilet									
			Sqm	1	15.00		2.10	31.50			
			Sqm	1	8.10		2.10	17.01			
		Total Executed Quantity						175.04			
		Tender Quantity						97.34			
		Quantity Upto 125%						121.68			
		Quantity Above 125%						53.37			
		Now to be Paid Quantity									
		Quantity Upto 125%						121.68	1782.21	216851.00	
		Quantity Above 125%						53.37	1388.59	74105.00	
Item No.21		Flooring with 25mm thick polished tandur blue stone slabs using cement mortar 1:6, 25mm thick over existing cement concrete bed or top of roof laid to line and level and jointed with cement slurry mixed with pigment to match the shade of the slab, including cost of materials, labour, curing, polishing complete as per specifications. As per the direction of the Engineer Incharge									
		Item Not Operated									
Item No.22		Providing and laying platform using prepolished, water cut I gang saw 40mm thick telephonic Black Granite. laid on existing vertical-supports and fixing in CM 1:3 proportion. Including cutting to required shape, pattern with paper joints, including full rounding for nosing, finished with cement mortar, pointed with colour pigments to match the colour of slab making through jointing with sealant, making holes 25mm x 12mm grooves in JOints including cost of all materials, mortar, labour, curing etc., complete as per specification.As per the direction of the Engineer Incharge									
		Item Not Operated									

A.E.E. (Project)

Executive Engineer Project Division Yelahanka Zone BBMP, Bangalore

RUDRAPRASAD CONSULTANTS BANGALORE

CONTRACTOR PMC ASSISTANT ENGINEER ASSISTANT EXECUTIVE ENGINEER

Scanned by TapScanner

Scanned by TapScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK:- Construction of Additional floor to existing Library at Vidyaranyapura Ward no.09 in Byatarayanapura Assembly Constituency

MEASUREMENT SHEET

Second & Final Bill

Client | **Sri. S K Keshavamurthy, #104, Sampigehalli, Jakkur Post, Bangalore-560064**

Chainage in m From	To	Description of Item	Unit	No	Length (m)	Breadth (m)	Depth (m)	Quantity	Rate Rs	Amount Rs	Remarks
Item No.23		Providing and fixing polished granite sink of size 60cms x 90cms of 23cm thick, the sink portion shall be 15cm in depth of shapes oval I round I square over brick masonry in cement mortar 1:6 including cost and conveyance of all materials, labour for all items of work, HOM with all lead and lift, loading and unloading, transportation charges and all other incidental charges etc., complete as per specification and directions of the Engineer-in-charge of the work.									
		Item Not Operated									
Item No.24		Providing Mathi/Nandi wood frames, wrought, framed or assembled including making plaster groves (excluding cost of cement concrete and side clamps), but including cost of materials, labour, HOM of machineries complete as per specifications.As per the direction of the Engineer Incharge									
Measurement Taken on		11/1/23 11/1/23									
		First Floor	Cum	1	6.92	0.14	0.08	0.08			
		Second Floor	Cum	1	6.92	0.14	0.08	0.08			
							Total Executed Quantity	**0.16**			
							Modified Schedule B Qty	**0.16**			
							Now to be Paid Quantity	**0.16**	**69164.36**	**10722.00**	
Item No.25		Providing and fixing in position fully panelled Honne wood shutters for doors, styles and rails of 30 mm. thick with bottom and lock rails 180 mm wide top rail and styles 100 mm wide as per drawing and panels of 25 mm thick including cost of materials.As per the direction of the Engineer Incharge									
Measurement Taken on		6/2/23 6/2/23									
			Sqm	1	1.36		1.92	2.61			
			Sqm	1	1.36		1.92	2.61			
							Total Executed Quantity	**5.22**			
							Modified Schedule B Qty	**5.22**			
							Now to be Paid Quantity	**5.22**	**4680.30**	**24443.00**	
Item No.26		KSRB 1.9 : Providing and fixing M.S.grill work for windows and ventilators using M.S. flats, or M.S. square rods, or combination of M.S. flats and square rods as per approved design, drawing including cutting steel sections and welding the same to required pattern with a coat of red lead primer, cost of materials, fixtures, labour and HOM complete as per specifications.PWD SR 2018-19, It No.7.10, Pg. No.34									
Measurement Taken on		6/2/23 6/2/23									
			Kgs								
		2nd Floor									
		Hall									
		W	Sqm	19	1.80		1.20	41.04			
		Gents Toilet									
		V	Sqm	1	1.30		0.43	0.56			
		V1	Sqm	1	0.65		0.45	0.29			
		Ladies Toilet									
		V	Sqm	1	0.63		0.42	0.26			
		V1	Sqm	1	1.25		0.42	0.53			
		V2	Sqm	1	0.60		0.60	0.36			
		1st Floor									
		Hall						51.30			
		W	Sqm	19	1.80		1.50				
		Gents Toilet						0.56			
		V	Sqm	1	1.30		0.43	0.29			
		V1	Sqm	1	0.65		0.45				
		Ladies Toilet						0.26			
		V	Sqm	1	0.63		0.42	0.53			
		V1	Sqm	1	1.25		0.42	0.36			
		V2	Sqm	1	0.60		0.60				

96.34

CONTRACTOR

RUDRAPRASAD GOPINATH CONSULTANTS BANGALORE PMC

Executive Engineer Project Division Yelahanka Zone BBMP Bangalore 30/1/2023

ASSISTANT ENGINEER

30/1/2023 A.E.E. (Project)

ASSISTANT EXECUTIVE ENGINEER

Scanned by TapScanner

Scanned by TapScanner
